ID	Resource Names	Activity	Project Name	SCH	Street	Post Code	Duration	Programme Start	Programme Finish	Design Drawing Measure
416		**Batch 6 - Operational Plan**					**407 days?**	**Mon 11/04/22**	**Mon 23/11/23**	**0**
5497		**LAMBETH**					**348.75 days**	**Tue 02/01/24**	**Fri 30/05/25**	**0**
5628	**Day Works**	**Scheme Level**	**DMR_7_10070 Coburg Crescent**				**110 days**	**Mon 19/02/24**	**Thu 25/07/24**	**252**
5629		**Street Level**	**DMR_7_10070 Coburg Crescent**	**SCH-00002509**	**Coburg Crescent**		**SW2 3EB 103 days**	**Mon 19/02/24**	**Tue 16/07/24**	**173**
5630		**Phase 1**	**DMR_7_10070 Coburg Crescent**		**Side of 129 - 14/15**		**24 days**	**Mon 19/02/24**	**Thu 21/03/24**	**0**
5631	Mains Team	Site Set up	DMR_7_10070 Coburg Crescent				3 days	Mon 19/02/24	Wed 21/02/24	0
5632	Mains Team	dig out trench for new main & new wash	DMR_7_10070 Coburg Crescent				4 days	Thu 22/02/24	Tue 27/02/24	0
5633	Drillers	Drill main	DMR_7_10070 Coburg Crescent				1 day	Wed 28/02/24	Wed 28/02/24	88
5634	NST	Shut at Point for connection	DMR_7_10070 Coburg Crescent		Detail 3		0.5 days	Thu 29/02/24	Thu 29/02/24	0
5635	Mains Team	Connection work at Point	DMR_7_10070 Coburg Crescent				1 day	Thu 29/02/24	Thu 29/02/24	0
5636	Testing Team	Presure test new pipework	DMR_7_10070 Coburg Crescent				0.5 days	Thu 29/02/24	Thu 29/02/24	0
5637	Testing Team	Cholinate and flush new pipework	DMR_7_10070 Coburg Crescent				2 days	Thu 29/02/24	Fri 01/03/24	0
5638	NST	Sample	DMR_7_10070 Coburg Crescent				1 day	Mon 04/03/24	Mon 04/03/24	0
5639	Mains Team	Service pipework lay and top tee install	DMR_7_10070 Coburg Crescent				4 days	Tue 05/03/24	Fri 08/03/24	0
5640	Supervisor	Awaiting results	DMR_7_10070 Coburg Crescent				5 days	Tue 05/03/24	Mon 11/03/24	0
5641	Mains Team	Connection pipework	DMR_7_10070 Coburg Crescent				1 day	Tue 12/03/24	Tue 12/03/24	0
5642	Mains Team	Service Transfers	DMR_7_10070 Coburg Crescent				3 days	Wed 13/03/24	Fri 15/03/24	0
5643	Grab & Mate	backfilling	DMR_7_10070 Coburg Crescent				2 days	Mon 18/03/24	Tue 19/03/24	0
5644	nstatement tea	reinstatement	DMR_7_10070 Coburg Crescent				1 day	Wed 20/03/24	Wed 20/03/24	0
5645	Back Up Driver	Site clear	DMR_7_10070 Coburg Crescent				1 day	Thu 21/03/24	Thu 21/03/24	0
5646		**Phase 2**	**DMR_7_10070 Coburg Crescent**		**14/15 - JW Palace Road**		**22 days**	**Thu 21/03/24**	**Tue 23/04/24**	**0**
5647	Mains Team	Site Set up	DMR_7_10070 Coburg Crescent				1 day	Thu 21/03/24	Thu 21/03/24	0
5648	Mains Team	dig out trench for new main & new wash	DMR_7_10070 Coburg Crescent				4 days	Fri 22/03/24	Wed 27/03/24	0
5649	Drillers	Drill main	DMR_7_10070 Coburg Crescent				1 day	Thu 28/03/24	Thu 28/03/24	85
5650	Testing Team	Presure test new pipework	DMR_7_10070 Coburg Crescent				0.5 days	Tue 02/04/24	Tue 02/04/24	0
5651	Testing Team	Cholinate and flush new pipework	DMR_7_10070 Coburg Crescent				2 days	Tue 02/04/24	Wed 03/04/24	0
5652	NST	Sample	DMR_7_10070 Coburg Crescent				1 day	Thu 04/04/24	Thu 04/04/24	0
5653	Mains Team	Service pipework lay and top tee install	DMR_7_10070 Coburg Crescent				4 days	Fri 05/04/24	Wed 10/04/24	0
5654	Supervisor	Awaiting results	DMR_7_10070 Coburg Crescent				5 days	Fri 05/04/24	Thu 11/04/24	0
5655	Mains Team	Connection pipework	DMR_7_10070 Coburg Crescent				1 day	Fri 12/04/24	Fri 12/04/24	0
5656	Mains Team	Service Transfers	DMR_7_10070 Coburg Crescent				3 days	Mon 15/04/24	Wed 17/04/24	0
5657	Grab & Mate	backfilling	DMR_7_10070 Coburg Crescent				2 days	Thu 18/04/24	Fri 19/04/24	0
5658	nstatement tea	reinstatement	DMR_7_10070 Coburg Crescent				1 day	Mon 22/04/24	Mon 22/04/24	0
5659	Back Up Driver	Site clear	DMR_7_10070 Coburg Crescent				1 day	Tue 23/04/24	Tue 23/04/24	0
5660		**Phase 5 - Abandonment**	**DMR_7_10070 Coburg Crescent**				**5 days**	**Wed 10/07/24**	**Tue 16/07/24**	**0**
5661	Mains Team	Site Set up	DMR_7_10070 Coburg Crescent				1 day	Wed 10/07/24	Wed 10/07/24	0
5662	NST	Abandonment shut	DMR_7_10070 Coburg Crescent				1 day	Thu 11/07/24	Thu 11/07/24	0
5663	Mains Team	Cut & Cap old main	DMR_7_10070 Coburg Crescent		Detail 3		1 day	Thu 11/07/24	Thu 11/07/24	0
5664	Grab & Mate	backfilling	DMR_7_10070 Coburg Crescent				1 day	Fri 12/07/24	Fri 12/07/24	0
5665	nstatement tea	reinstatement	DMR_7_10070 Coburg Crescent				1 day	Mon 15/07/24	Mon 15/07/24	0
5666	Back Up Driver	Site clear	DMR_7_10070 Coburg Crescent				1 day	Tue 16/07/24	Tue 16/07/24	0
5667		**Street Level**	**DMR_7_10070 Coburg Crescent**	**SCH-00002893**	**Palace Road**		**SW2 3EB 66 days**	**Tue 23/04/24**	**Thu 25/07/24**	**79**
5668		**Phase 3**	**DMR_7_10070 Coburg Crescent**		**Coburg Crescent - Hillside Road**		**23 days**	**Tue 23/04/24**	**Fri 24/05/24**	**0**
5669	Mains Team	Site Set up	DMR_7_10070 Coburg Crescent				1 day	Tue 23/04/24	Tue 23/04/24	0
5670	Mains Team	dig out trench for new main & new wash	DMR_7_10070 Coburg Crescent				6 days	Wed 24/04/24	Wed 01/05/24	60
5671	NST	Shut at Point for connection	DMR_7_10070 Coburg Crescent		Detail 2		0.5 days	Thu 02/05/24	Thu 02/05/24	0
5672	Mains Team	Connection work at Point	DMR_7_10070 Coburg Crescent				1 day	Thu 02/05/24	Thu 02/05/24	0
5673	Testing Team	Presure test new pipework	DMR_7_10070 Coburg Crescent				0.5 days	Thu 02/05/24	Thu 02/05/24	0
5674	Testing Team	Cholinate and flush new pipework	DMR_7_10070 Coburg Crescent				2 days	Thu 02/05/24	Fri 03/05/24	0
5675	NST	Sample	DMR_7_10070 Coburg Crescent				1 day	Tue 07/05/24	Tue 07/05/24	0
5676	Mains Team	service pipework lay and top tee install	DMR_7_10070 Coburg Crescent				4 days	Wed 08/05/24	Mon 13/05/24	0
5677	Supervisor	Awaiting results	DMR_7_10070 Coburg Crescent				5 days	Wed 08/05/24	Tue 14/05/24	0
5678	Mains Team	Connection pipework	DMR_7_10070 Coburg Crescent				1 day	Wed 15/05/24	Wed 15/05/24	0
5679	Mains Team	Service Transfers	DMR_7_10070 Coburg Crescent				3 days	Thu 16/05/24	Mon 20/05/24	0
5680	Grab & Mate	backfilling	DMR_7_10070 Coburg Crescent				2 days	Tue 21/05/24	Wed 22/05/24	0
5681	nstatement tea	reinstatement	DMR_7_10070 Coburg Crescent				1 day	Thu 23/05/24	Thu 23/05/24	0
5682	Back Up Driver	Site clear	DMR_7_10070 Coburg Crescent				1 day	Fri 24/05/24	Fri 24/05/24	0
5683		**Phase 4**	**DMR_7_10070 Coburg Crescent**				**25 days**	**Fri 24/05/24**	**Fri 28/06/24**	**0**
5684	Mains Team	Site Set up	DMR_7_10070 Coburg Crescent				1 day	Fri 24/05/24	Fri 24/05/24	0
5685	Mains Team	dig out trench for new main & new wash	DMR_7_10070 Coburg Crescent				2 days	Tue 28/05/24	Wed 29/05/24	12
5686	Grab & Mate	backfil	DMR_7_10070 Coburg Crescent				2 days	Thu 30/05/24	Fri 31/05/24	0
5687	Reinstatement	reinstate	DMR_7_10070 Coburg Crescent				1 day	Mon 03/06/24	Mon 03/06/24	0
5688	TM	swap TM	DMR_7_10070 Coburg Crescent				1 day	Tue 04/06/24	Tue 04/06/24	0
5689	Mains Team	dig out trench for new main & new wash	DMR_7_10070 Coburg Crescent				2 days	Wed 05/06/24	Thu 06/06/24	7
5690	NST	Shut at Point for connection	DMR_7_10070 Coburg Crescent		Detail 1		0.5 days	Fri 07/06/24	Fri 07/06/24	0
5691	Mains Team	Connection work at Point	DMR_7_10070 Coburg Crescent				1 day	Fri 07/06/24	Fri 07/06/24	0
5692	Testing Team	Presure test new pipework	DMR_7_10070 Coburg Crescent				0.5 days	Fri 07/06/24	Fri 07/06/24	0
5693	Testing Team	Cholinate and flush new pipework	DMR_7_10070 Coburg Crescent				2 days	Fri 07/06/24	Mon 10/06/24	0
5694	NST	Sample	DMR_7_10070 Coburg Crescent				1 day	Tue 11/06/24	Tue 11/06/24	0
5695	Mains Team	Service pipework lay and top tee install	DMR_7_10070 Coburg Crescent				4 days	Wed 12/06/24	Mon 17/06/24	0
5696	Supervisor	Awaiting results	DMR_7_10070 Coburg Crescent				5 days	Wed 12/06/24	Tue 18/06/24	0
5697	Mains Team	Connection pipework	DMR_7_10070 Coburg Crescent				1 day	Wed 19/06/24	Wed 19/06/24	0
5698	Mains Team	Service Transfers	DMR_7_10070 Coburg Crescent				3 days	Thu 20/06/24	Mon 24/06/24	0
5699	Grab & Mate	backfilling	DMR_7_10070 Coburg Crescent				2 days	Tue 25/06/24	Wed 26/06/24	0
5700	nstatement tea	reinstatement	DMR_7_10070 Coburg Crescent				1 day	Thu 27/06/24	Thu 27/06/24	0
5701	Back Up Driver	Site clear	DMR_7_10070 Coburg Crescent				1 day	Fri 28/06/24	Fri 28/06/24	0
5702	NST	Abandone	DMR_7_10070 Coburg Crescent				1 day	Tue 25/06/24	Tue 25/06/24	0
5703	Supervisor	Abandone	DMR_7_10070 Coburg Crescent				10 days	Wed 26/06/24	Tue 09/07/24	0
5704		**Phase 5 - Abandonment**	**DMR_7_10070 Coburg Crescent**				**10 days**	**Fri 12/07/24**	**Thu 25/07/24**	**0**
5705	Mains Team	Site Set up	DMR_7_10070 Coburg Crescent				1 day	Fri 12/07/24	Fri 12/07/24	0
5706	NST	Abandonment shut	DMR_7_10070 Coburg Crescent				1 day	Mon 15/07/24	Mon 15/07/24	0
5707	Mains Team	Cut & Cap old main	DMR_7_10070 Coburg Crescent		Detail 2		1 day	Mon 15/07/24	Mon 15/07/24	0
5708	Grab & Mate	backfilling	DMR_7_10070 Coburg Crescent				1 day	Tue 16/07/24	Tue 16/07/24	0
5709	nstatement tea	reinstatement	DMR_7_10070 Coburg Crescent				1 day	Wed 17/07/24	Wed 17/07/24	0
5710	Back Up Driver	Site clear	DMR_7_10070 Coburg Crescent				1 day	Thu 18/07/24	Thu 18/07/24	0
5711	Mains Team	Site Set up	DMR_7_10070 Coburg Crescent				1 day	Fri 19/07/24	Fri 19/07/24	0
5712	NST	Abandonment shut	DMR_7_10070 Coburg Crescent				1 day	Mon 22/07/24	Mon 22/07/24	0
5713	Mains Team	Cut & Cap old main	DMR_7_10070 Coburg Crescent		Detail 1		1 day	Mon 22/07/24	Mon 22/07/24	0
5714	Grab & Mate	backfilling	DMR_7_10070 Coburg Crescent				1 day	Tue 23/07/24	Tue 23/07/24	0
5715	nstatement tea	reinstatement	DMR_7_10070 Coburg Crescent				1 day	Wed 24/07/24	Wed 24/07/24	0
5716	Back Up Driver	Site clear	DMR_7_10070 Coburg Crescent				1 day	Thu 25/07/24	Thu 25/07/24	0

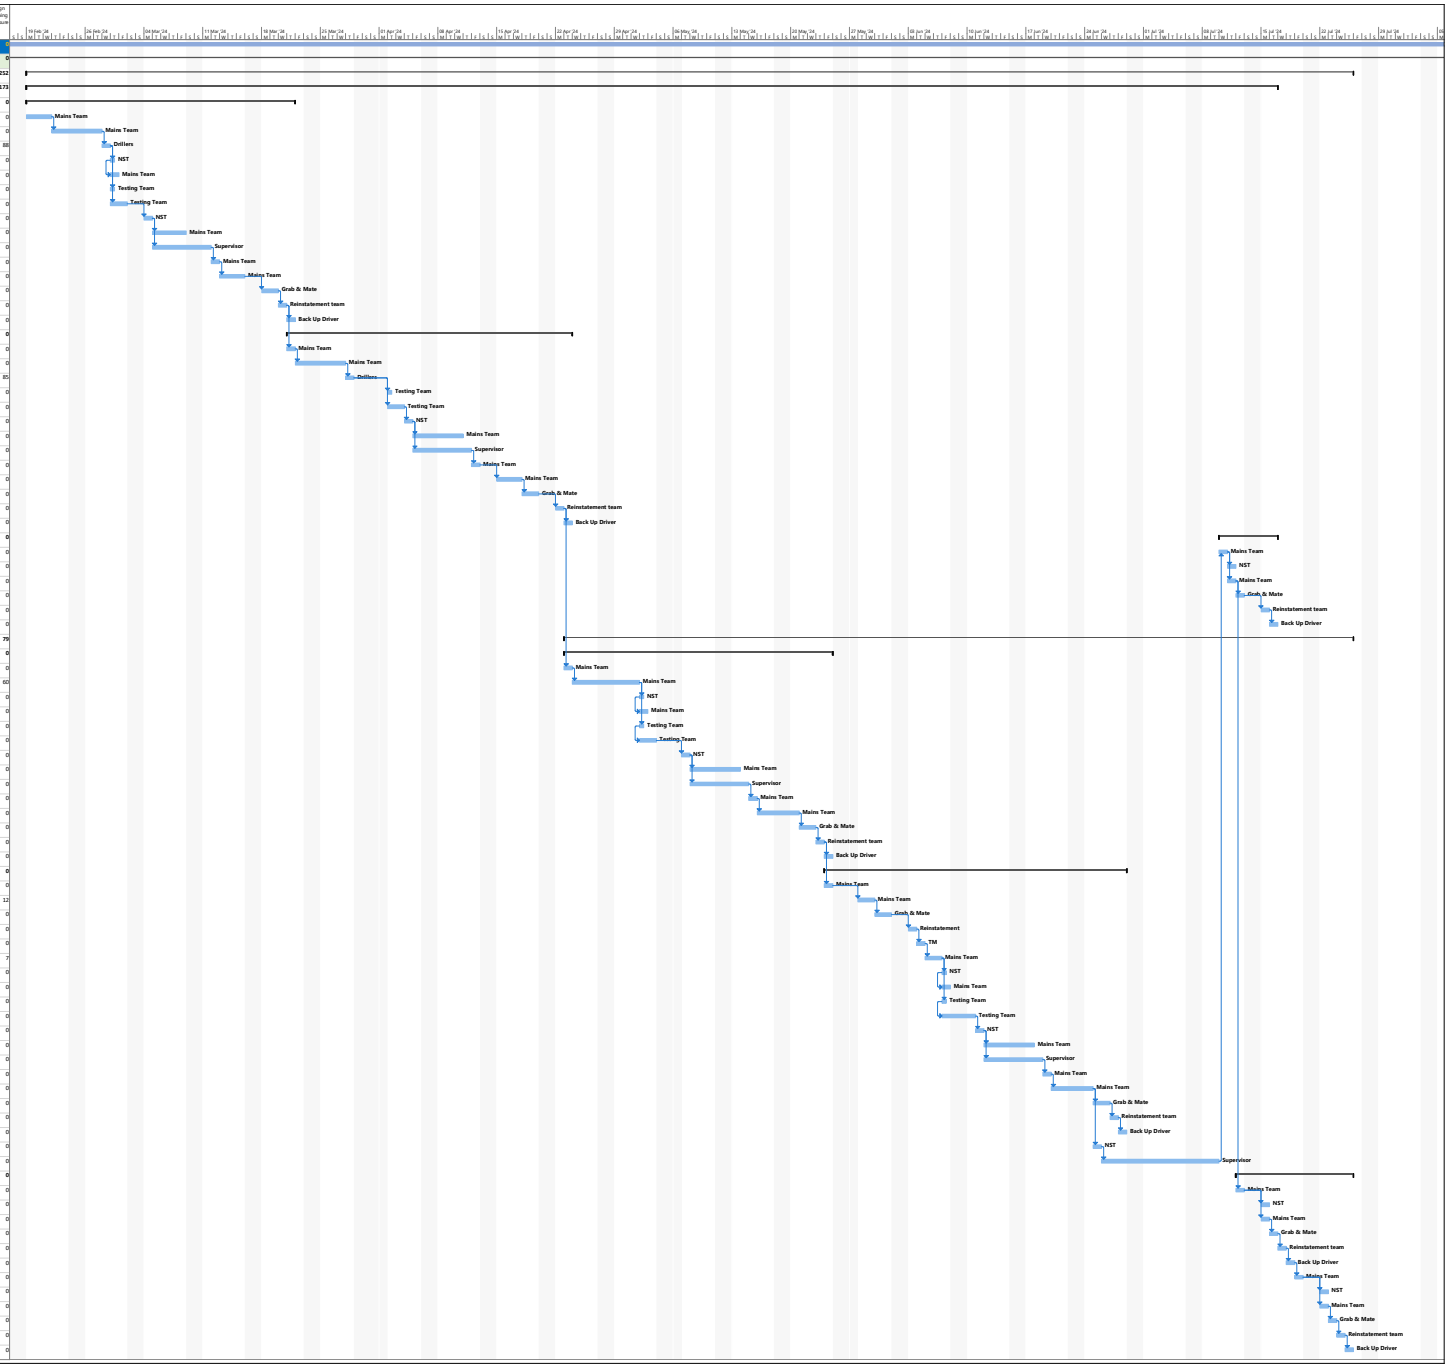

Project: AMP7 - programme - B
Date: Mon 06/11/23

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Progress | Manual Progress
